



# ***Whittier Bridge/I-95 Improvement Project***

## ***Tri - Town Working Group Meeting***

***July 10, 2017***

## **Agenda**

- **Introductions**
- **Status**
- **2017 Work**
  - **Whittier Bridge Construction**
  - **Roadwork**
- **Milestones**
  - **2017**
  - **Completion**
- **Questions and Answers**

# Status

- SB Pier 1 ongoing
- SB arch steel erection complete
- North end roadway work complete
- Minor Bridge work complete this month
- Two of four river piers removed




## 2017 Work

SPAN 1 AND 2 STEEL AND  
PRECAST DECK

PARAPETS

HIGHWAY  
LIGHTING

TRAIL  
HEADS

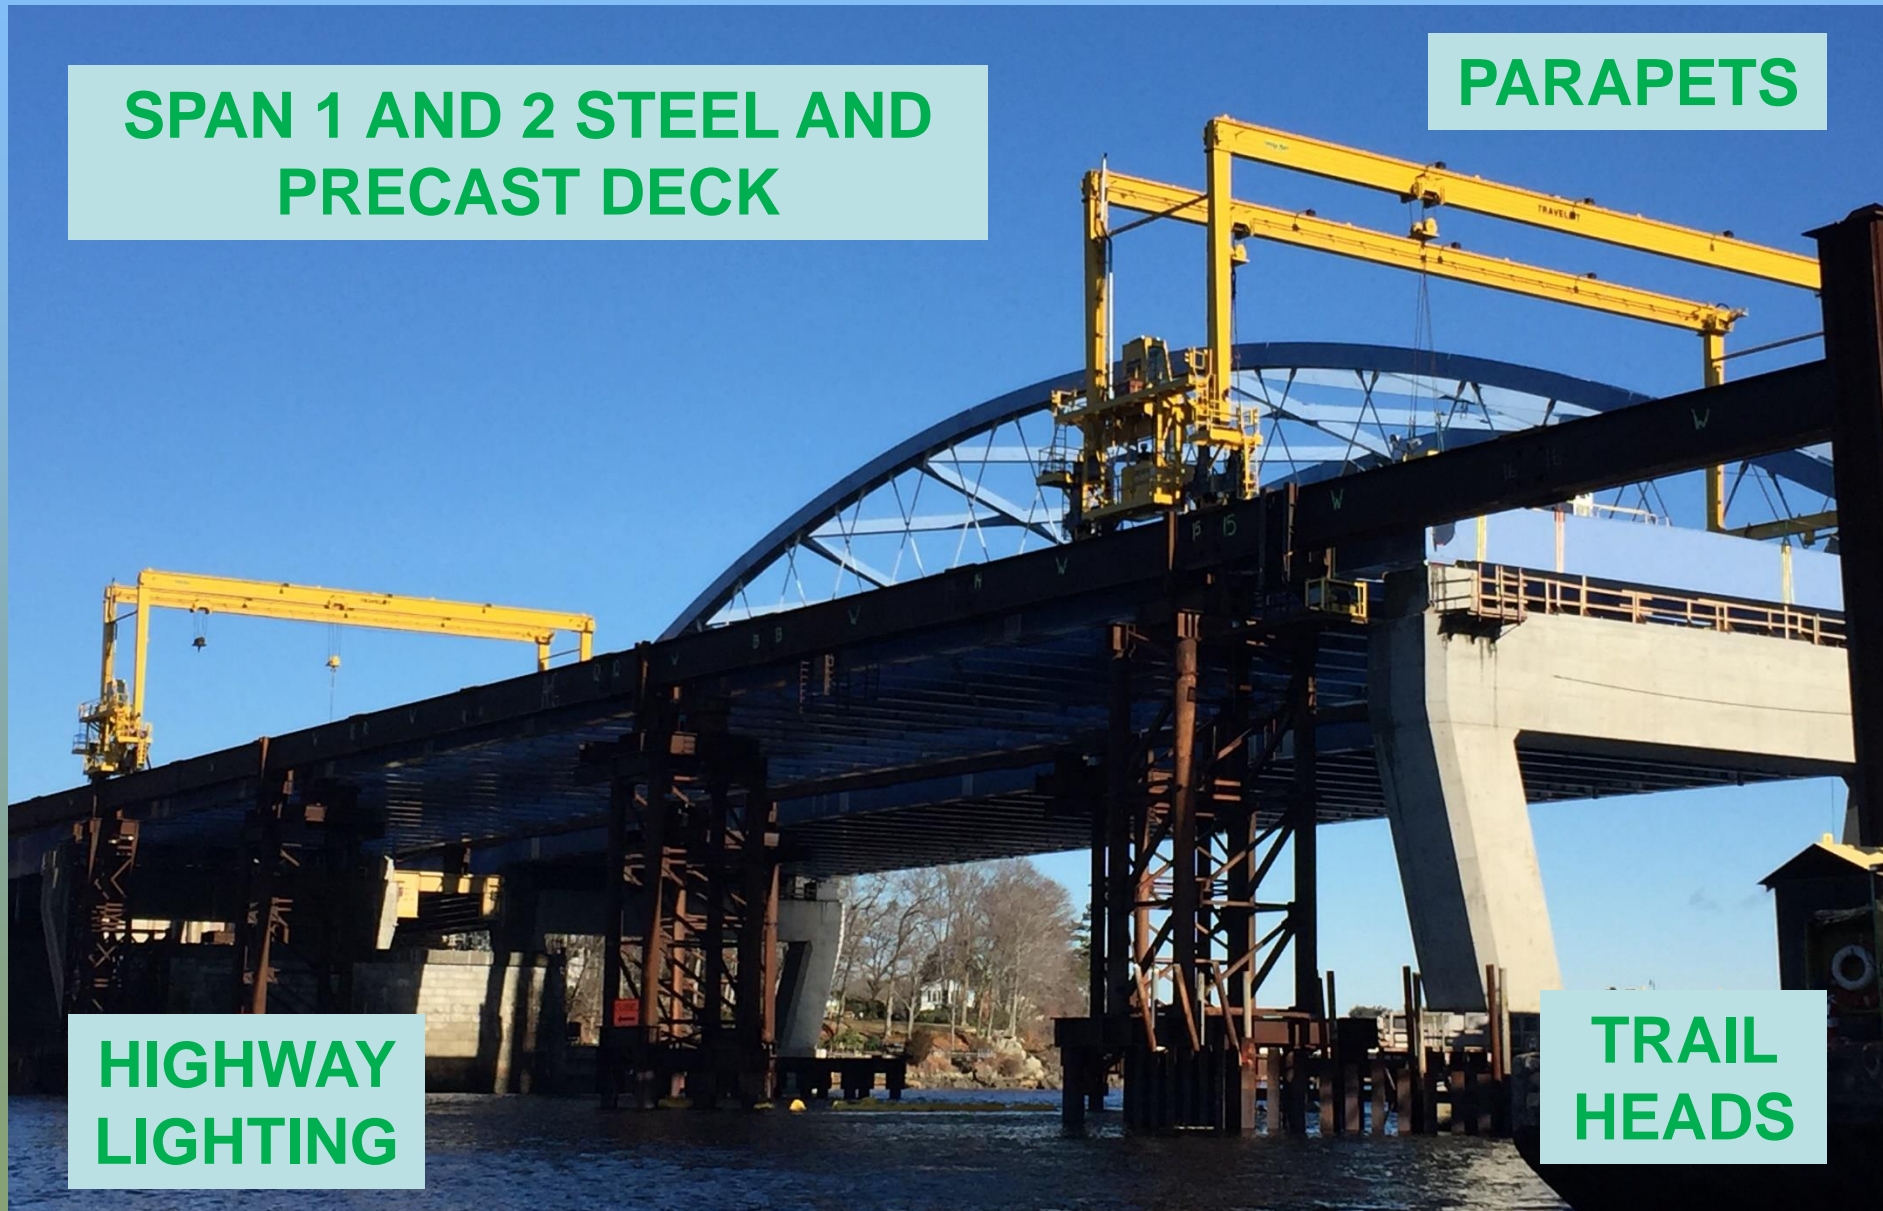

# 2018 Work

**CROSS-OVER REMOVALS**

**FINAL  
PAVING**

**FINAL IN-WATER  
REMOVALS**

**SHARED  
USE PATH**






## SOUTHBOUND WHITTIER BRIDGE 2017 / 2018

- **PIER 1 SB**
- **SPAN 1&2**
- **STEEL**
- **PRECAST**
- **DECK**
- **ARCH**
- **HANGERS**
- **BARRIERS**
- **REMOVALS**




# WHITTIER BRIDGE / I-95 IMPROVEMENT PROJECT

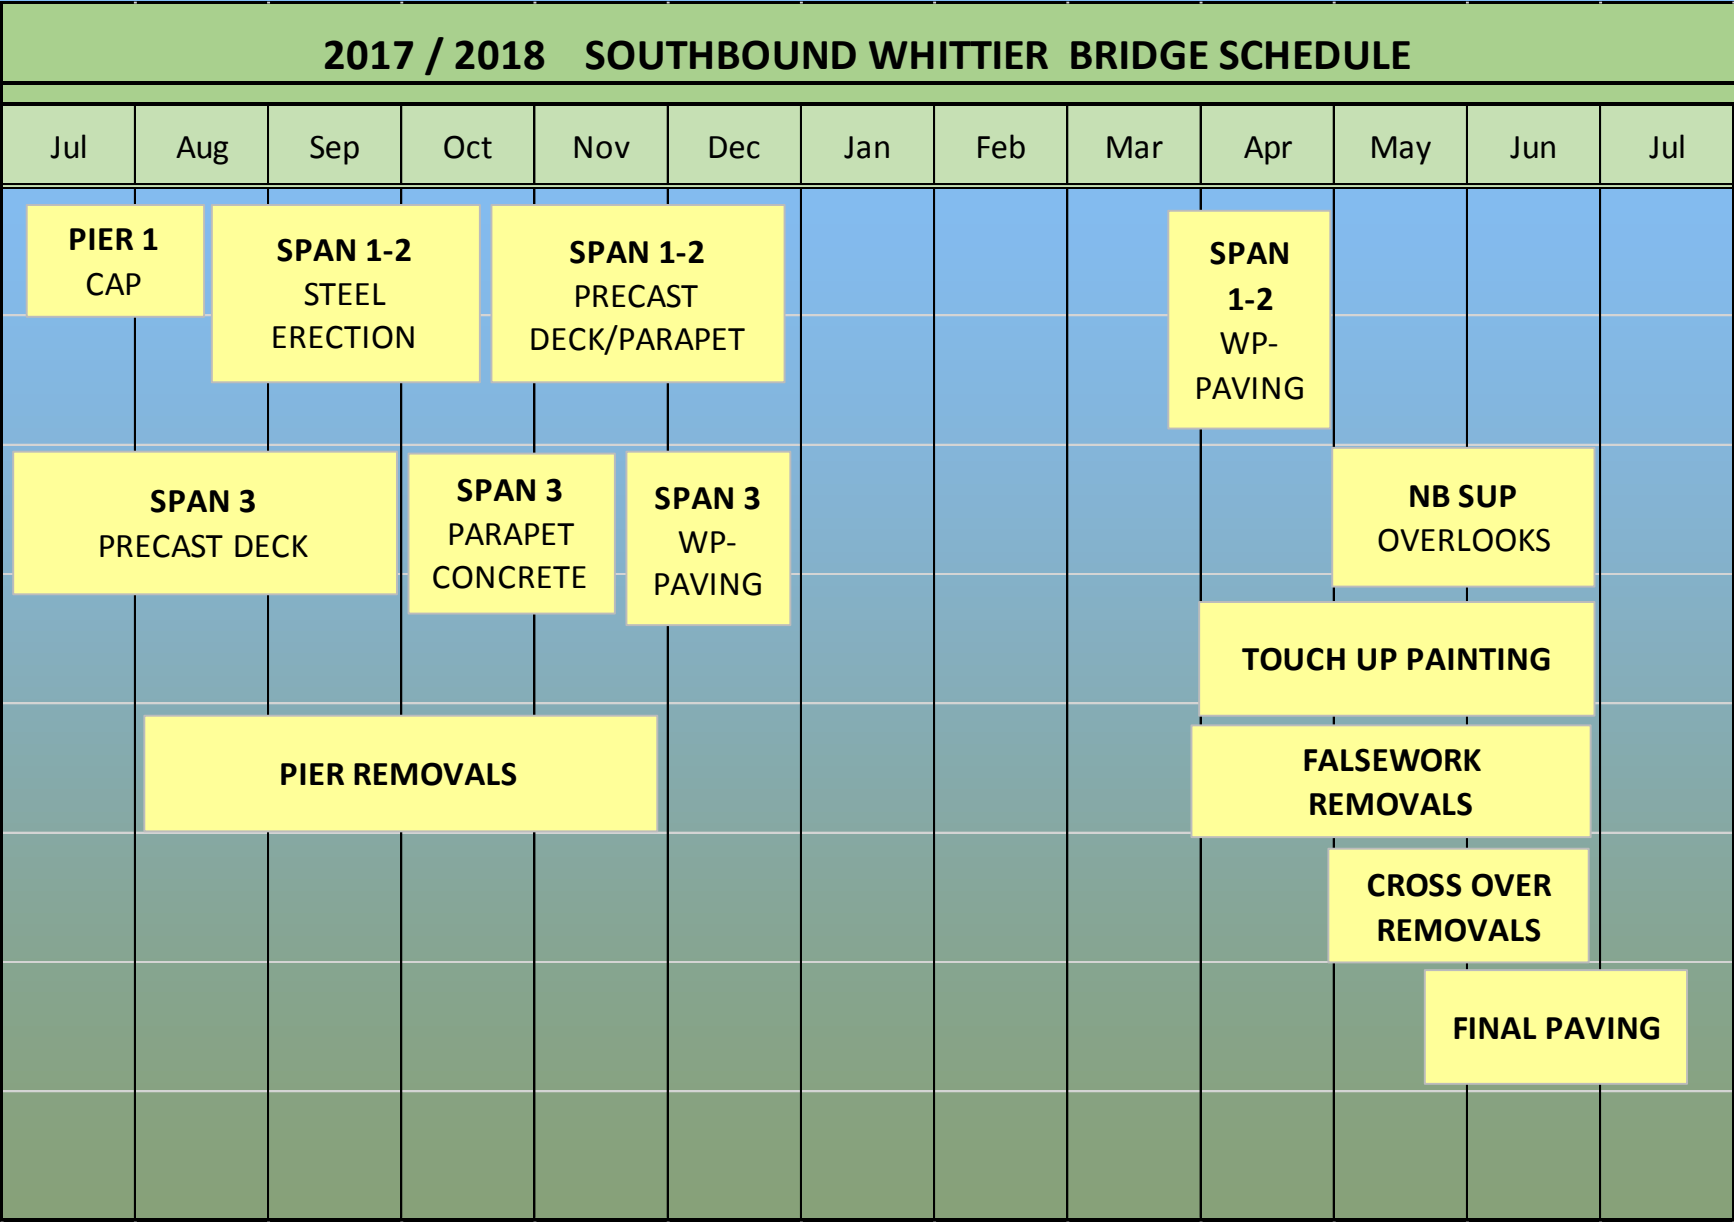

# SUPERSTRUCTURE WORK

- **Steel Erection**
- **Precast Slabs**
- **Post Tensioning**
- **Concrete Barriers**
- **Hangers**

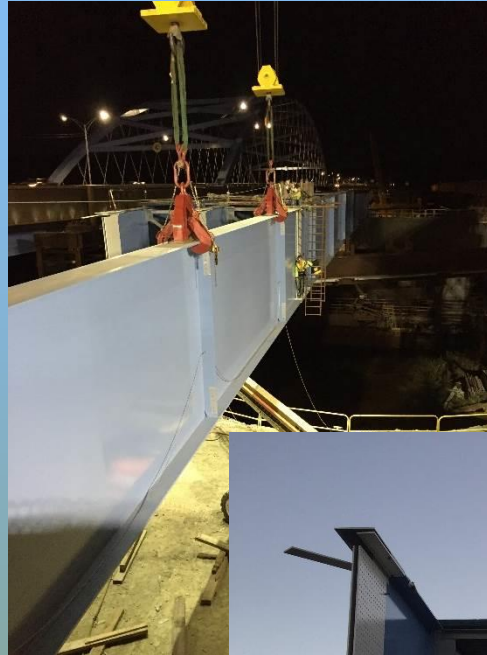



## COMPLETION WORK

- **Falsework Removals**
- **Pier Removals**
- **Steel Painting**
- **SUP Barrier**
- **Overlooks**



# WHITTIER BRIDGE / I-95 IMPROVEMENT PROJECT



**Route 110 Overpass Painting**

# ROADWAY

- **Wall Facings**
- **ITS Systems**
- **Surface Course Paving**
- **Lighting**
- **Pavement Markings**
- **Signage**
- **Interpretive Signs**



# WHITTIER BRIDGE / I-95 IMPROVEMENT PROJECT



**Shared Use Path (SUP)**

## **Hours of Work**

- **Whittier Bridge - 2 shifts of extended work hours 6 days / week**
- **Night operations**
  - **Concrete Placements**
  - **Steel Erection**
  - **Paving**
  - **Striping**
  - **Overhead Signs**

## MILESTONES

- 2017 Milestone
  - North End Roadway – Complete
- 2018 Milestones
  - SB Whittier Bridge Opening – April 2018
  - Final Completion – July 2018
